

To John Hunt

Rpt. 6.

For the information of Surveyors and the Committee only.

Received at

Office,

10

Lloyd's Register of Shipping.

(Report on Vessel No. 38644 Port Glasgow)

No. 16446. SHIP FORGINGS OR CASTINGS

I have to report that the undermentioned ~~Iron or Steel Forgings or Castings~~, manufactured by Emerson Walker & Thompson Ltd. of Dunston-on-Tyne for the Vessel No. 261, being built by J. Fullerton & Co. Ltd. of Glasgow have been inspected by me as set forth below and found to be, so far as can be seen, Sound

New Spk. as per Plan

Mark on Forgings or Castings.

Lloyd's



No. 3614N

W. Campbell

Newcastle

	STERN FRAME.	RUDDER FRAME.	STEM.
Material*	Scrap Steel	Scrap Steel	
How made	Forged & Smithed	Forged & Machined	
Dimensions	5 3/4 x 5 1/2 x 3	4 1/4	
Progress on Inspection	Finished	Finished	
Date when Inspected	July 10, to December 19-1918.		
CASTINGS.			
Tests on Standard Test Pieces.			
Tensile Test—			
Tons per square inch			
Extension per cent. ...			
Cold Bending Test—			
Angle before fracture			
Drop Test—			
Height from ground ...			
Hammering Test—			
If made according to Rules and found satisfactory ...			

SKETCHES OF FRAMES SHOWING POSITION AND DESCRIPTION OF WELDS OF FORGINGS.

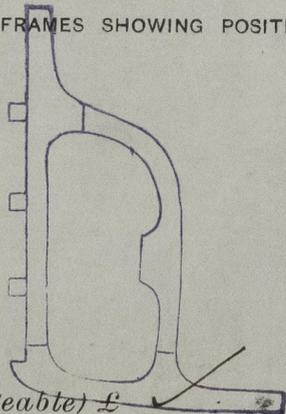

Fee (if any chargeable) £

To be paid at



Lloyd's Register Foundation
