

Verification Report

Index No.

(For London Office only.)

Lloyd's Register of Shipping.

SURVEYS FOR FREEBOARD-STEAM SHIPS.

PARTICULARS RELATING TO ALL STEAM SHIPS EITHER FLUSH DECKED, OR WITH TOP GALLANT FORECASTLES, SHORT POOPS AND BRIDGE HOUSES DISCONNECTED, OR WITH TOP GALLANT FORECASTLES HAVING LONG POOPS, OR RAISED QUARTER DECKS CONNECTED WITH BRIDGE HOUSES, OR OTHERWISE.

Port of Survey *San Francisco*Date of Survey *while building*Name of Surveyor *ALW. R. Rab*

Ship's Name	Port of Registry and Nationality	Official Number	Gross Tonnage	Date of Build	Particulars of Classification
<i>S.S. BIRKENHEAD</i> <i>Moore & Co. No 166</i>	<i>New York</i>	<i>10091</i>	<i>1921</i>	<i>1921</i>	<i>Carrying petroleum in bulk (contemplated)</i>

Registered dimensions from ship's Register.	LENGTH.	BREADTH.	DEPTH.	UNDER DECK TONNAGE.
	<i>425.0</i>	<i>57.20</i>	<i>33.10</i>	<i>6433</i>
Length on LOADLINE.		Frame Depth <i>9.20</i>	Ceiling + <i>20</i>	Peak
		Rule <i>62</i>	Sheer + <i>1.21</i>	Tanks + <i>50</i>
CORRECTED DIMENSIONS.	<i>425.0</i>	<i>57.08</i>	<i>34.51</i>	<i>6483</i>

Moulded Depth as measured..... *33' 0"*Addition for Keel below base line for draught record..... *2 3/8* inches.

NOTE. — If the depth is measured when vessel is afloat, the details of measurement should be reported.

CORRECTION FOR LENGTH.

Length of Ship on Loadline.....	<i>425.0</i>
Length in Table	<i>396.0</i>
Difference	<i>29.0</i>
Correction for 10ft., Table A.	<i>1.6</i>
× Difference divided by 10	<i>4.64</i>
If 1/10ths length covered divide by 2	<i>+ 4 3/4</i>

CORRECTION FOR IRON DECK.

Proportion covered, if less than 1/10ths length covered	<i>4564</i>
Thickness of usual wood deck, less stringer	<i>- 1 1/2</i>

CORRECTION FOR ROUND OF BEAM.

Breadth at Gunwale amidships.....	<i>56.0</i>
Round of Beam	<i>14</i>
Normal round.....	<i>14</i>
Difference	<i>0</i>
Proportion of Deck uncovered (Para. 19)	<i>0</i>

NOTE. — The round of beam should be reported on the full breadth of vessel at the gunwale.

Co-efficient of fineness.....	<i>77.78</i>
Any modification necessary {	
Para. 4 (a) to (e)*	
Co-efficient as corrected	<i>77</i>

Sheer { Stem..... <i>127</i>	<i>183</i> ÷ 2 = <i>91.5</i> Mean
at { Sternpost .. <i>56</i>	
Sheer at 1/8 of the length from { Stem <i>78</i>	<i>106</i> ÷ 2 = <i>53</i> Mean
{ Sternpost .. <i>28</i>	
Gradual mean Sheer	<i>93.93</i> ÷ 33 = <i>96.36</i>
Standard mean Sheer [Table, Para. 18]	<i>52.50</i>
Difference.....	<i>41.43</i> ÷ 4 = <i>10.35</i>
§ If limited as Para. 18 (f)	<i>- 10 1/4</i>

Rise in Sheer { At front of bridge house.....	<i>✓</i>
from amidships {	
[Para. 18 (e)] { At after end of forecastle	<i>✓</i>

Fall in Sheer {	÷ 2 =
Para. 18 (d) {	
Length uncovered	<i>✓</i>
Correction	

ALLOWANCE FOR DECK ERECTIONS:—	
Freeboard, Table C.....	<i>5.45</i>
Correction for Length, if required (Para. 12, 13, and 14)	<i>+ 2.32</i>
Freeboard by Table A. corrected for sheer, and for length, if required (Para. 12, 13, and 14)	<i>8.44</i>
Difference	<i>2.59</i>
Percentage as below.....	<i>28.94</i>

Correction for R. Q. Dk. if engine and boiler openings not covered by bridge house (Para. 11)	<i>8.67</i>
Allowance for Deck Erections	<i>- 8 3/4</i>

Length.	Length allowed.	Height.
Forecastle..... <i>41.25</i>	<i>41.25</i>	<i>8.0</i>
Bridge House..... <i>36.5</i>	<i>47.00</i>	<i>8.0</i>
† Raised Qr. Dk.....		
Poop..... <i>105.75</i>	<i>105.75</i>	
Total	<i>194.00</i>	
Length of Ship	<i>425.00</i>	<i>4564</i>

Corresponding percentage {	
(Para. 11, 12, 13, or 14) {	<i>28.94</i>

FREEBOARD recommended amidships from centre of Disc to top of Statutory Deck Line, Wood (Iron) Deck:—

Fresh Water Line	above centre of Disc	...
Indian Summer Line	"	...
Winter Line	below	...
Winter North Atlantic Line	"	...

† If the frames, skin planking, or ceiling are of unusual thickness the breadth of vessel to inside of ceiling should be reported if possible.

† In vessels obtaining an allowance for deck erections under Para. 11 where the sheer drops abaft amidships the height of the R.Q.D. is to be taken from the level of the top of the amidship beam.

§ In flush-decked vessels the total standard mean sheer means the sheer measured at the stem and sternpost. In vessels having poops and forecastles, it means the sheer measured at points distant one-eighth of the vessel's length from stem and sternpost.

+ State dimensions of freeing port area on back of this form.

The Surveyor should state whether the fall in sheer as reported is measured relatively to the straight line of keel or to the water line. If measured relatively to water line the surveyor must state the time of survey, and also the usual load and forward and aft should be reported.

MARKING REPORT
RECEIVED 19/10/21

W1006-2106

Do all the Frames extend to the top height in the Poop? *yes*
 To what height do the Reverse Frames extend? *Longitudinal framing*
 Has the Poop or Raised Quarter Deck an efficient Iron Bulkhead at the fore end? *yes*
 Give particulars of the means for closing the openings in Bulkhead *Water-tight steel doors*
 Is the Poop or Raised Quarter Deck connected with the Bridge House? *no*
 Give particulars of the means for closing the openings in Bulkhead *Water-tight steel doors*
 What is the thickness of the Bridge Front plating? *7/16* and Coaming plate? *1/2"*
 Give scantlings and spacing of the Stiffeners *8 x 3.41 x 3.41 x 48 channels spaced about 3' 0" apart*
 Are bracket plates fitted at each end of the Stiffeners? *yes*
 Has the Bridge House an efficient Iron Bulkhead at the after end? *yes*
 How are the openings closed? *Hinged steel doors*
 Is the Forecastle at least as high as the main or top-gallant rail? *yes*
 Are the Engine and Boiler openings covered by a Bridge, Poop, Raised Quarter Deck, or enclosed by a Strong Iron or Steel Deckhouse? *yes*
 If the openings are not so protected are the exposed parts of the Casings efficiently constructed? *yes*
 Give thickness of plating; scantlings and spacing of Stiffeners *yes*
 What is the height of the exposed Casings? *yes*
 Are suitable means provided for closing all openings in them in bad weather? *yes*
 Are the Weather Deck Hatchways efficiently constructed and at least equal to the requirements of Section 28 of the Rules for 1904-5? Give particulars below:— *yes*

Position and Size.		Ship.	Rule.	Ship.	Rule.	Ship.	Rule.	Ship.	Rule.
COAMING.	Height above top of DECK	<i>24</i>		<i>22</i>	<i>oil hatchways 6' 0" x 4' 0"</i>				
	Thickness { Sides.....	<i>44</i>		<i>10</i>		<i>"</i>	<i>4' 0" x 2' 4"</i>		
	Ends.....	<i>44</i>							
SHIFTING BEAMS OR WEB PLATES.	Number	<i>one</i>							
	Section and Scantlings	<i>Plate 12 x 3/8</i>							
	Material	<i>angle 3 x 3 x 7/16</i>							
* FORE AND AFTERS.	Number								
	Section and Scantlings	<i>✓</i>							
	Material								
HATCHES Thickness		<i>3</i>							
Remarks.....		<i>solid</i>							

* The depth of Fore and Afters should be stated from the underside of the hatches in all cases.


(If the sill of the lowest side scuttle will be less than 6 inches above the Indian Summer Load Line if assigned under the tables, state vertical distance from top of deck at side amidships to lower edge of lowest side scuttle.)

The following information is to be given in all Cases of vessels dealt with under Paras. 11, 12 (under 15 feet Moulded depth) and under Shelter Deck Rules.

What is the thickness of the Bridge Sheerstrake? _____
 Delete the words { The Crew are, are not, berthed in the bridge house.
 that do not apply { The arrangements to enable them to get backwards and forwards from their quarters are, are not satisfactory.

Length of Bulwarks in well

Area of Freeing Ports required by Para. 11 (e) each side of vessel			=	Sq. ft.
Ft. Tenth.	Ft. Tenth.	No.	}	
x	x			
x	x			
Freeing Ports (each side of vessel)			=	Sq. ft.
Total deficiency or excess			=	Sq. ft.

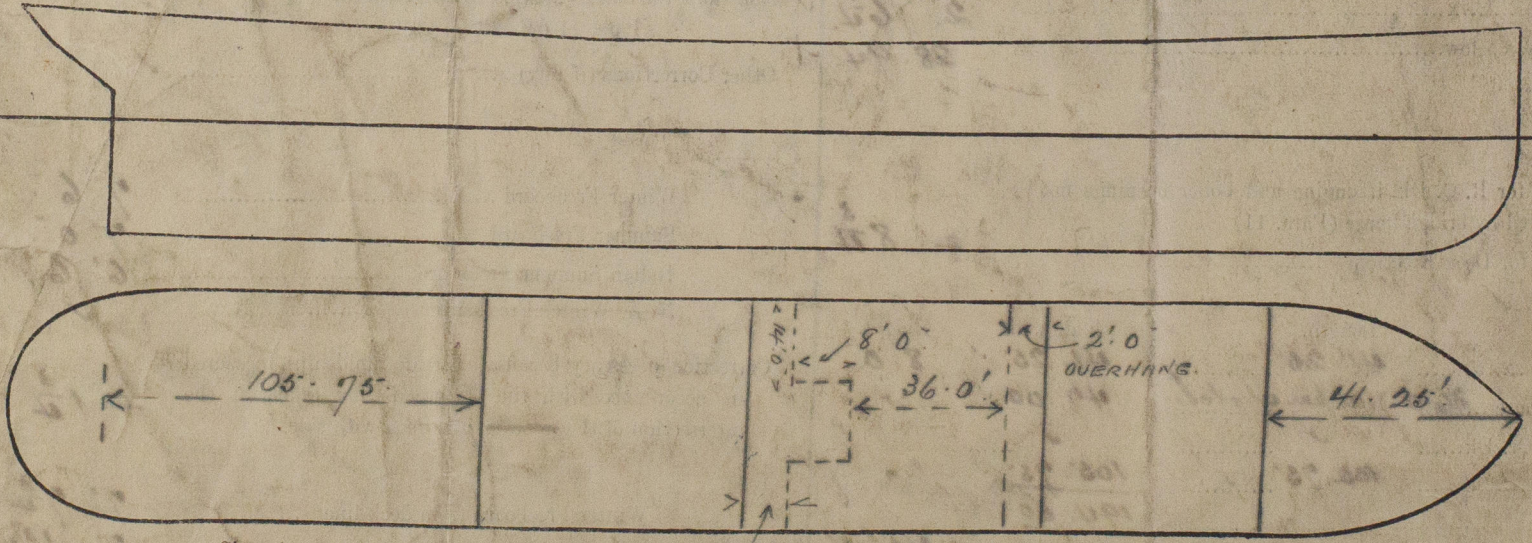

Show hereon line of Floors or Tank Top with position of any Breaks in same; also height of Peak Tank tops, &c., &c.

State any special features in the construction of the Vessel *Sister vessel to S/S 'GARGOYLE' SFO. RPT No 3429*
except that the under-deck tonnage has been measured in accordance with the latest ruling for Isherwood tank vessels. The Builder signs the favour of an early reply.

Owners _____
 Address _____

Fee \$ *100.00*

Received by me

